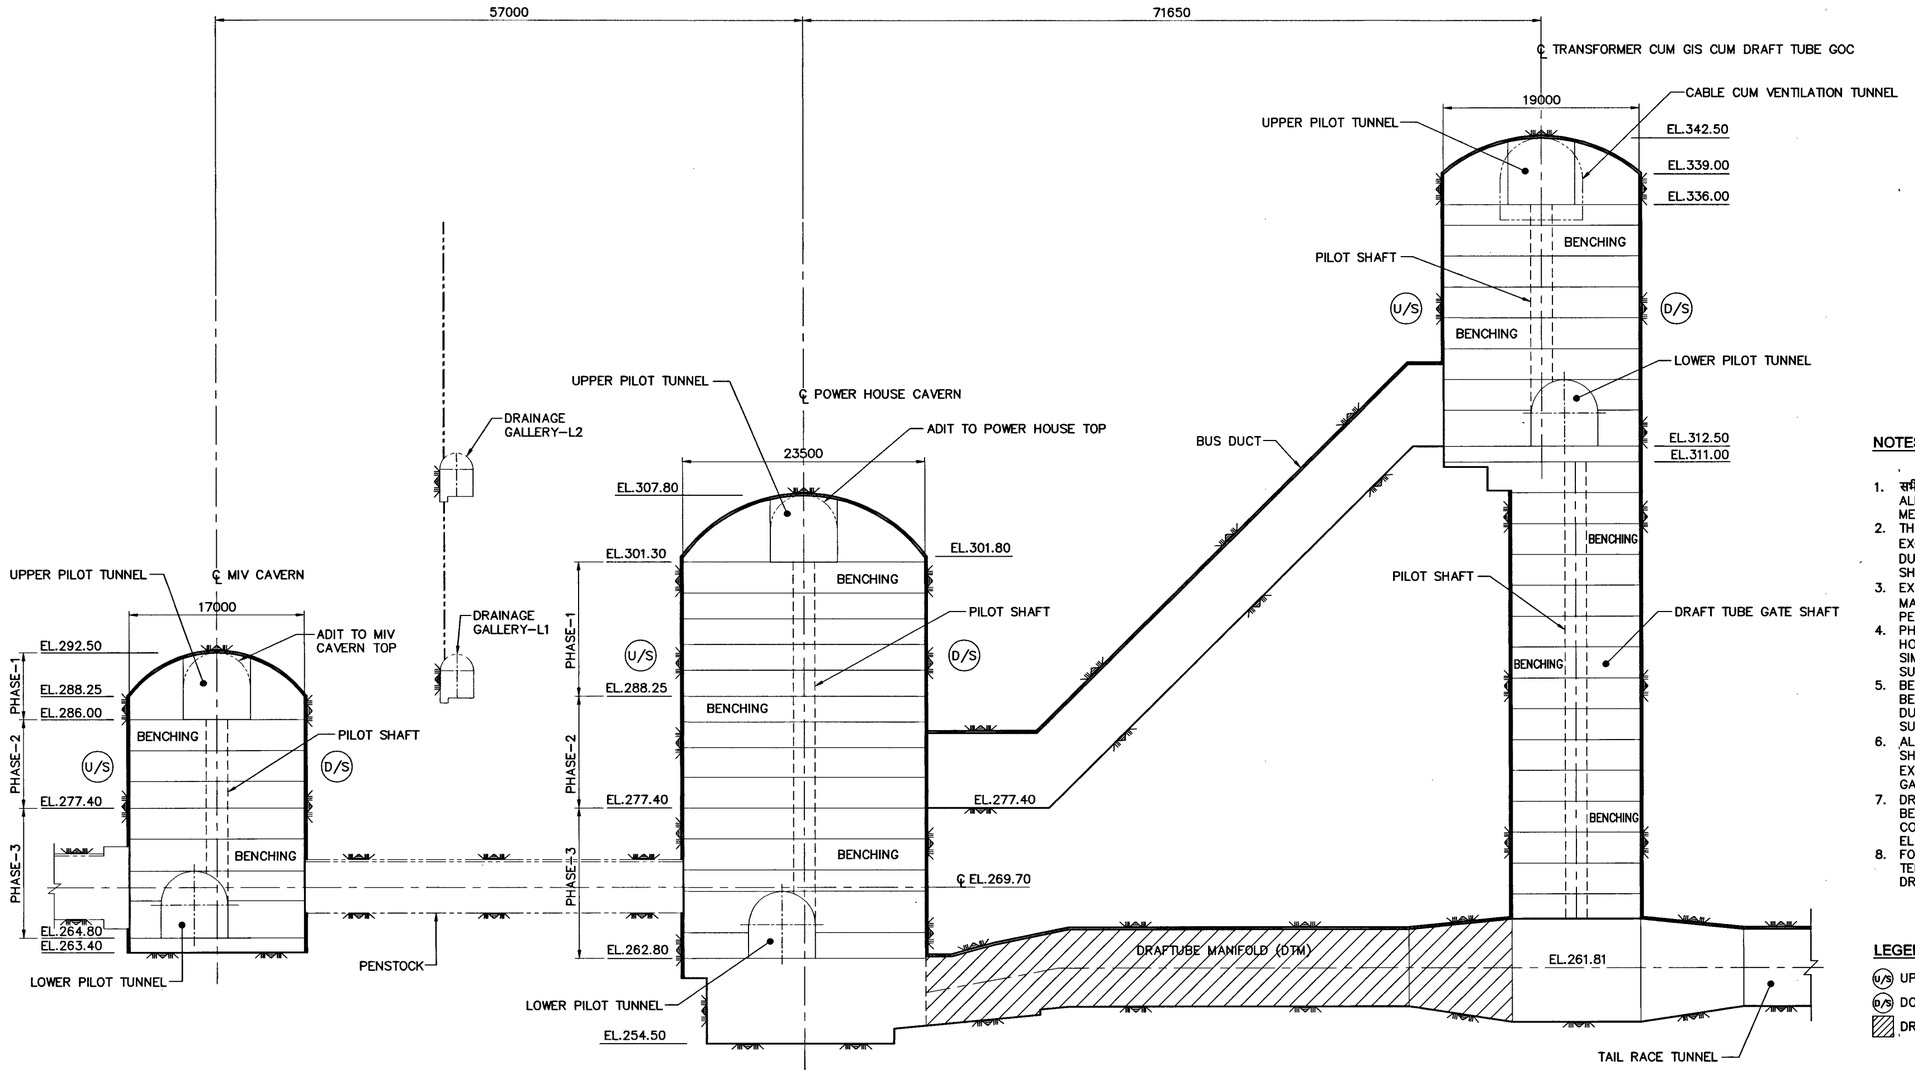


NOTES:-

1. सभी माप मिलीमीटर में तथ ऊंचाई मीटर में दिए गए है।
 ALL DIMENSIONS ARE IN MILLIMETRE AND ELEVATIONS IN METRE.
2. THIS IS SCHEMATIC ARRANGEMENT OF INTERDEPENDENT EXCAVATION SEQUENCE FOR CAVERNS/BUS DUCTS/DRAFT TUBE MANIFOLDS/DRAFT TUBE GATE SHAFTS.
3. EXCAVATION OF CAVERNS/BUS DUCTS/DRAFT TUBE MANIFOLDS/DRAFT TUBE GATE SHAFTS SHALL BE AS PER SECTION B.3 OF TECHNICAL SPECIFICATIONS.
4. PHASE–2 & PHASE–3 OF MIV CAVERN AND POWER HOUSE CAVERN SHALL BE BENCHED DOWN SIMULTANEOUSLY WITH THE INSTALLATION OF ROCK SUPPORTS INCLUDING TENDONS.
5. BEFORE BENCHING DOWN OF POWER HOUSE CAVERN BELOW EL.277.40, LOWER HORIZONTAL PORTION OF BUS DUCT AT EL.277.40 SHALL BE EXCAVATED AND SUPPORTED.
6. ALTERNATE BUS DUCTS/DRAFT TUBE GATE SHAFTS SHALL BE EXCAVATED AND SUPPORTED PRIOR TO EXCAVATION OF INTERMEDIATE BUS DUCT/DRAFT TUBE GATE SHAFT AND INSTALLATION OF TENDONS.
7. DRAFT TUBE MANIFOLD (ZONE MARKED AS DTM) SHALL BE EXCAVATED AFTER EXCAVATION AND ROCK SUPPORT COMPLETION OF BUS DUCTS AND POWER HOUSE UP TO EL 262.80.
8. FOR EXCAVATION AND ROCK SUPPORTS INCLUDING TENDONS OF INDIVIDUAL STRUCTURES, REFER SEPARATE DRAWINGS.

LEGENDS:-

- (U/S) UPSTREAM SIDE
- (D/S) DOWNSTREAM SIDE
- DRAFT TUBE MANIFOLD (DTM)

REFERENCE DRAWINGS:-

1. NHDB–4AC4–41–DD–0001.

SCALE:

0 4.0 8.0 12.0 16.0 20.0 METRE

एन एच पी सी लिमिटेड
(भारत सरकार का उद्यम)
NHPC Limited
(A GOVT. OF INDIA ENTERPRISE)

दिबांग बहुउद्देशीय परियोजना
DIBANG MULTIPURPOSE PROJECT

POWER HOUSE COMPLEX CAVERNS / BUS DUCTS / DRAFT TUBE MANIFOLDS / DRAFT TUBE GATE SHAFTS EXCAVATION SEQUENCE (SCHEMATIC)

DATE	NO.	REVISION OR ISSUES	BY	CH.	APP.
20.02.2026	00	ISSUED FOR CONSTRUCTION			

DESIGN MEMO NO. डिजाइन मेमो संख्या

DRAWN अंकित DEEPAK | SUBMITTED प्रस्तुत PRABHAT ASWAL | RECOMMENDED अनुशंसित NITISH RANJAN KUMAR | DEM / HM | APPROVED अनुमोदन SUDARSHAN

DATE दिनांक	DRG. NO. ड्रेग संख्या					
FEB 2026	NHDB	4AC4	41	DD	1003	00

DRG. NO. NHDB-4AC4-41-DD-1003-00

IMS/OED/F-02 REV. NO. : 03 EFF. DATE 21.07.2016
